


Tree Protection Note:

The applicant is responsible for ensuring that tree protection hoarding is maintained throughout all phases of demolition and construction in the location and condition as approved by the Planning and Building Department. No materials (building materials, soil, etc.) may be stockpiled within the area of hoarding. Failure to maintain the hoarding as originally approved or the storage of materials within the hoarding will be cause for the Letter of Credit to be held for two years following completion of all site works. Hoarding must be inspected prior to the removal of any tree hoarding from the site.

Owner's Signature: _____


Date: _____

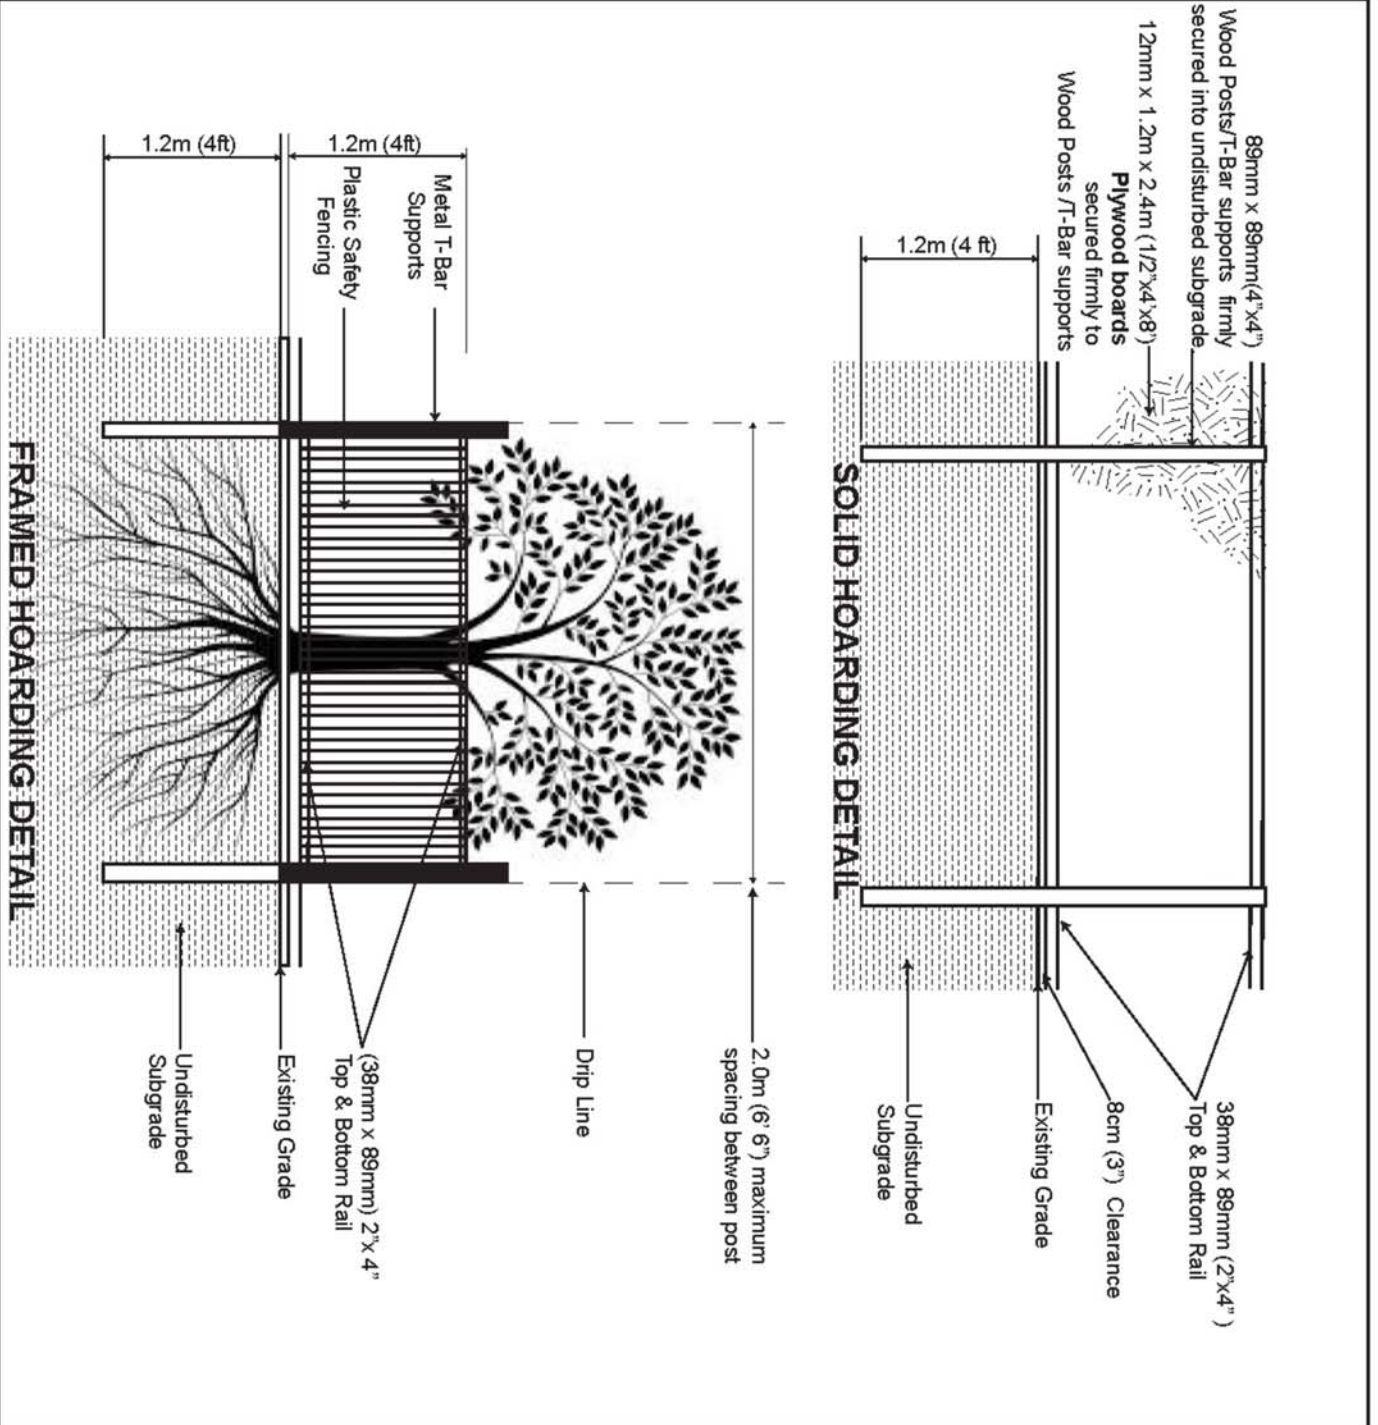

NOTES:

1. Hoarding details to be determined following initial site inspection.
2. Private tree hoarding to be approved by Development & Design.
3. City tree hoarding to be approved by Community Services Department throughout all phases of construction.
4. Inspection must be conducted by the Development and Design Division prior to removing any/all private hoarding.
5. Do not allow water to collect and pond behind or within hoarding.
6. Plywood must be utilized for solid hoarding. OSB/Chipboard will not be accepted for solid hoarding. Plywood sheets must be installed on construction side of frame.
7. Applicant is responsible to ensure utility locates are completed within city boulevard prior to installing framed hoarding.

TREE PRESERVATION HOARDING

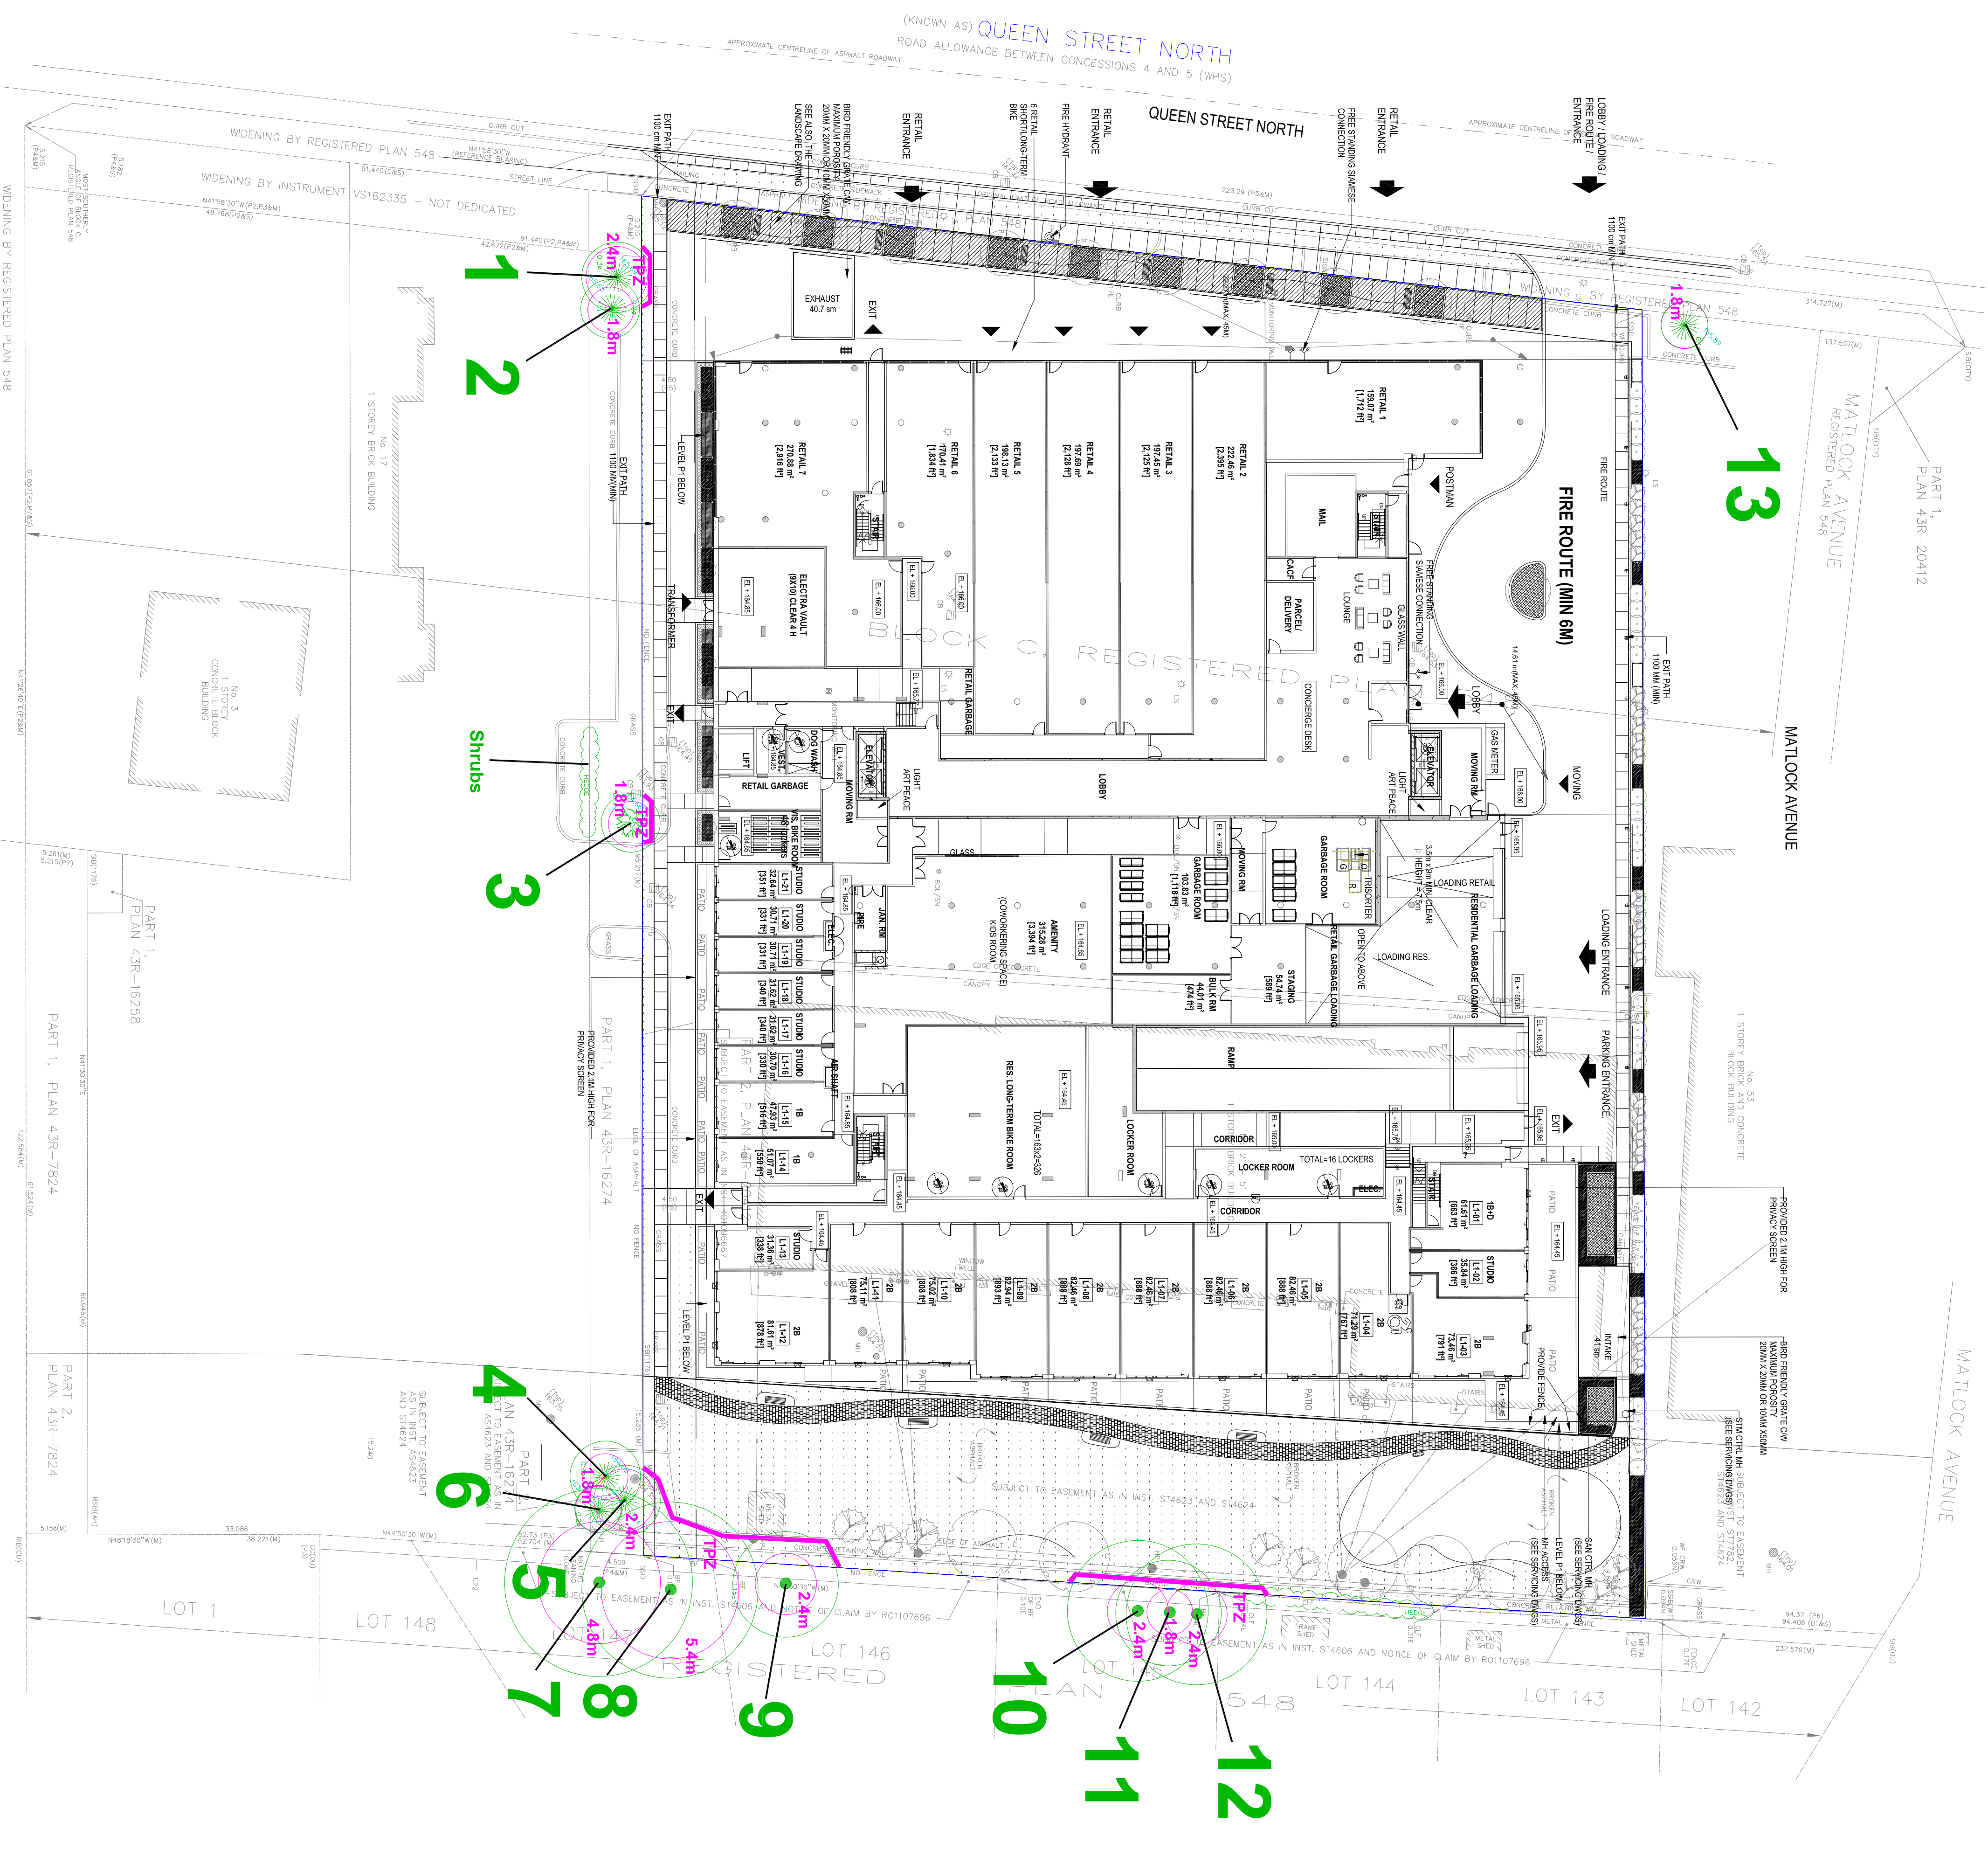

LEGEND

- Tree Inventory**
- Refer to Table 1 of report dated 7 September 2021 and revised 21 July 2023 for tree inventory information. Trees greater than 10cm DBH on and within 6M metres of the subject property were included in the inventory.
- Tree Removals**
- No trees are required to be removed to accommodate the proposed development.
- Tree Preservation**
- The preservation of all trees will be possible with appropriate tree protection measures. Trees identified for preservation are indicated with GREEN labels. Tree protection measures will have to be implemented prior to construction. Required tree preservation fencing is indicated in MAGENTA. Refer to Tree Protection Plan Notes for preservation details and tree preservation fence detail.
- Tree label (GREEN), preservation recommended: **X**
 - Dipline (GREEN CIRCLE)
 - Minimum tree protection zone (MAGENTA CIRCLE), with radius as measured from edge of tree in metres: **xm**
 - Surveyed coniferous tree:
 - Surveyed deciduous tree:
 - Tree location estimated by KFCI:
 - Location of required tree preservation fencing (thick MAGENTA):

Specifications for the Protection and Preservation of Existing Vegetation

- The following notes are to be included on all tree preservation plans:
1. All existing trees, which are to remain, shall be fully protected with hoarding to City standards, erected beyond their "drop line" prior to the issuance of the Erosion and Sediment Control Permit, to the satisfaction of the Community Services Department. Groups of trees and other existing plantings to be protected, shall be treated in a like manner with hoarding around the entire clump(s). Areas within the protective hoarding shall remain undisturbed and shall not be used for the storage of building materials or equipment.
 2. No rigging cables shall be wrapped around or installed in trees. Surplus soil, equipment, debris or materials shall not be placed over root systems of the trees within the protective fencing. No contaminants will be dumped or flushed where feeder roots of trees exist.
 3. The developer or his/her agents shall take every precaution necessary to prevent damage to trees or shrubs to be retained.
 4. Where limbs or portions of trees are removed to accommodate construction work, they will be removed carefully in accordance with accepted arboricultural practices.
 5. Where root systems of trees are exposed directly adjacent to or damaged by construction work, they shall be trimmed neatly and the area backfilled with appropriate material to prevent desiccation.
 6. Where necessary, the trees will be given an overall pruning to restore the balance between roots and top growth or to restore the appearance of the trees.
 7. Trees that have died or have been damaged beyond repair, shall be removed and replaced by the owner at the developer's own expense with trees of a size and species as approved by the Community Services Department.
 8. If grades around trees to be protected are likely to change, the owner shall be required to submit a plan to the City showing the proposed grading and root leading, to the satisfaction of the Community Services Department.

No.	Issue/Revisions	Date	By
1	Report Submission	7 Sept. 2021	KHH
2	Report Revision	21 Jul. 2023	KHH

Base Data: KFCI/CAH Surveys Ltd. (099); Lamb Development Corp. (Site files)

KUNTZ FORESTRY CONSULTING INC.

1461 Lakeshore Road West
 PO Box 7287 Lakeshore W/PO
 Oakville ON L6K 0B3
 T: 289.537.1871
 e: consultant@kuntzforestry.ca
 web: www.kuntzforestry.ca

Client: **Lamb Development Corp.**
 778 King Street West
 Toronto, Ontario M5C 1N6

Property: **21 - 51 Queen Street North**
 Mississauga, Ontario

Tree Inventory and Preservation Plan

Project	P2884	Figure	1
Date	7 September 2021		
Scale	1:300		
